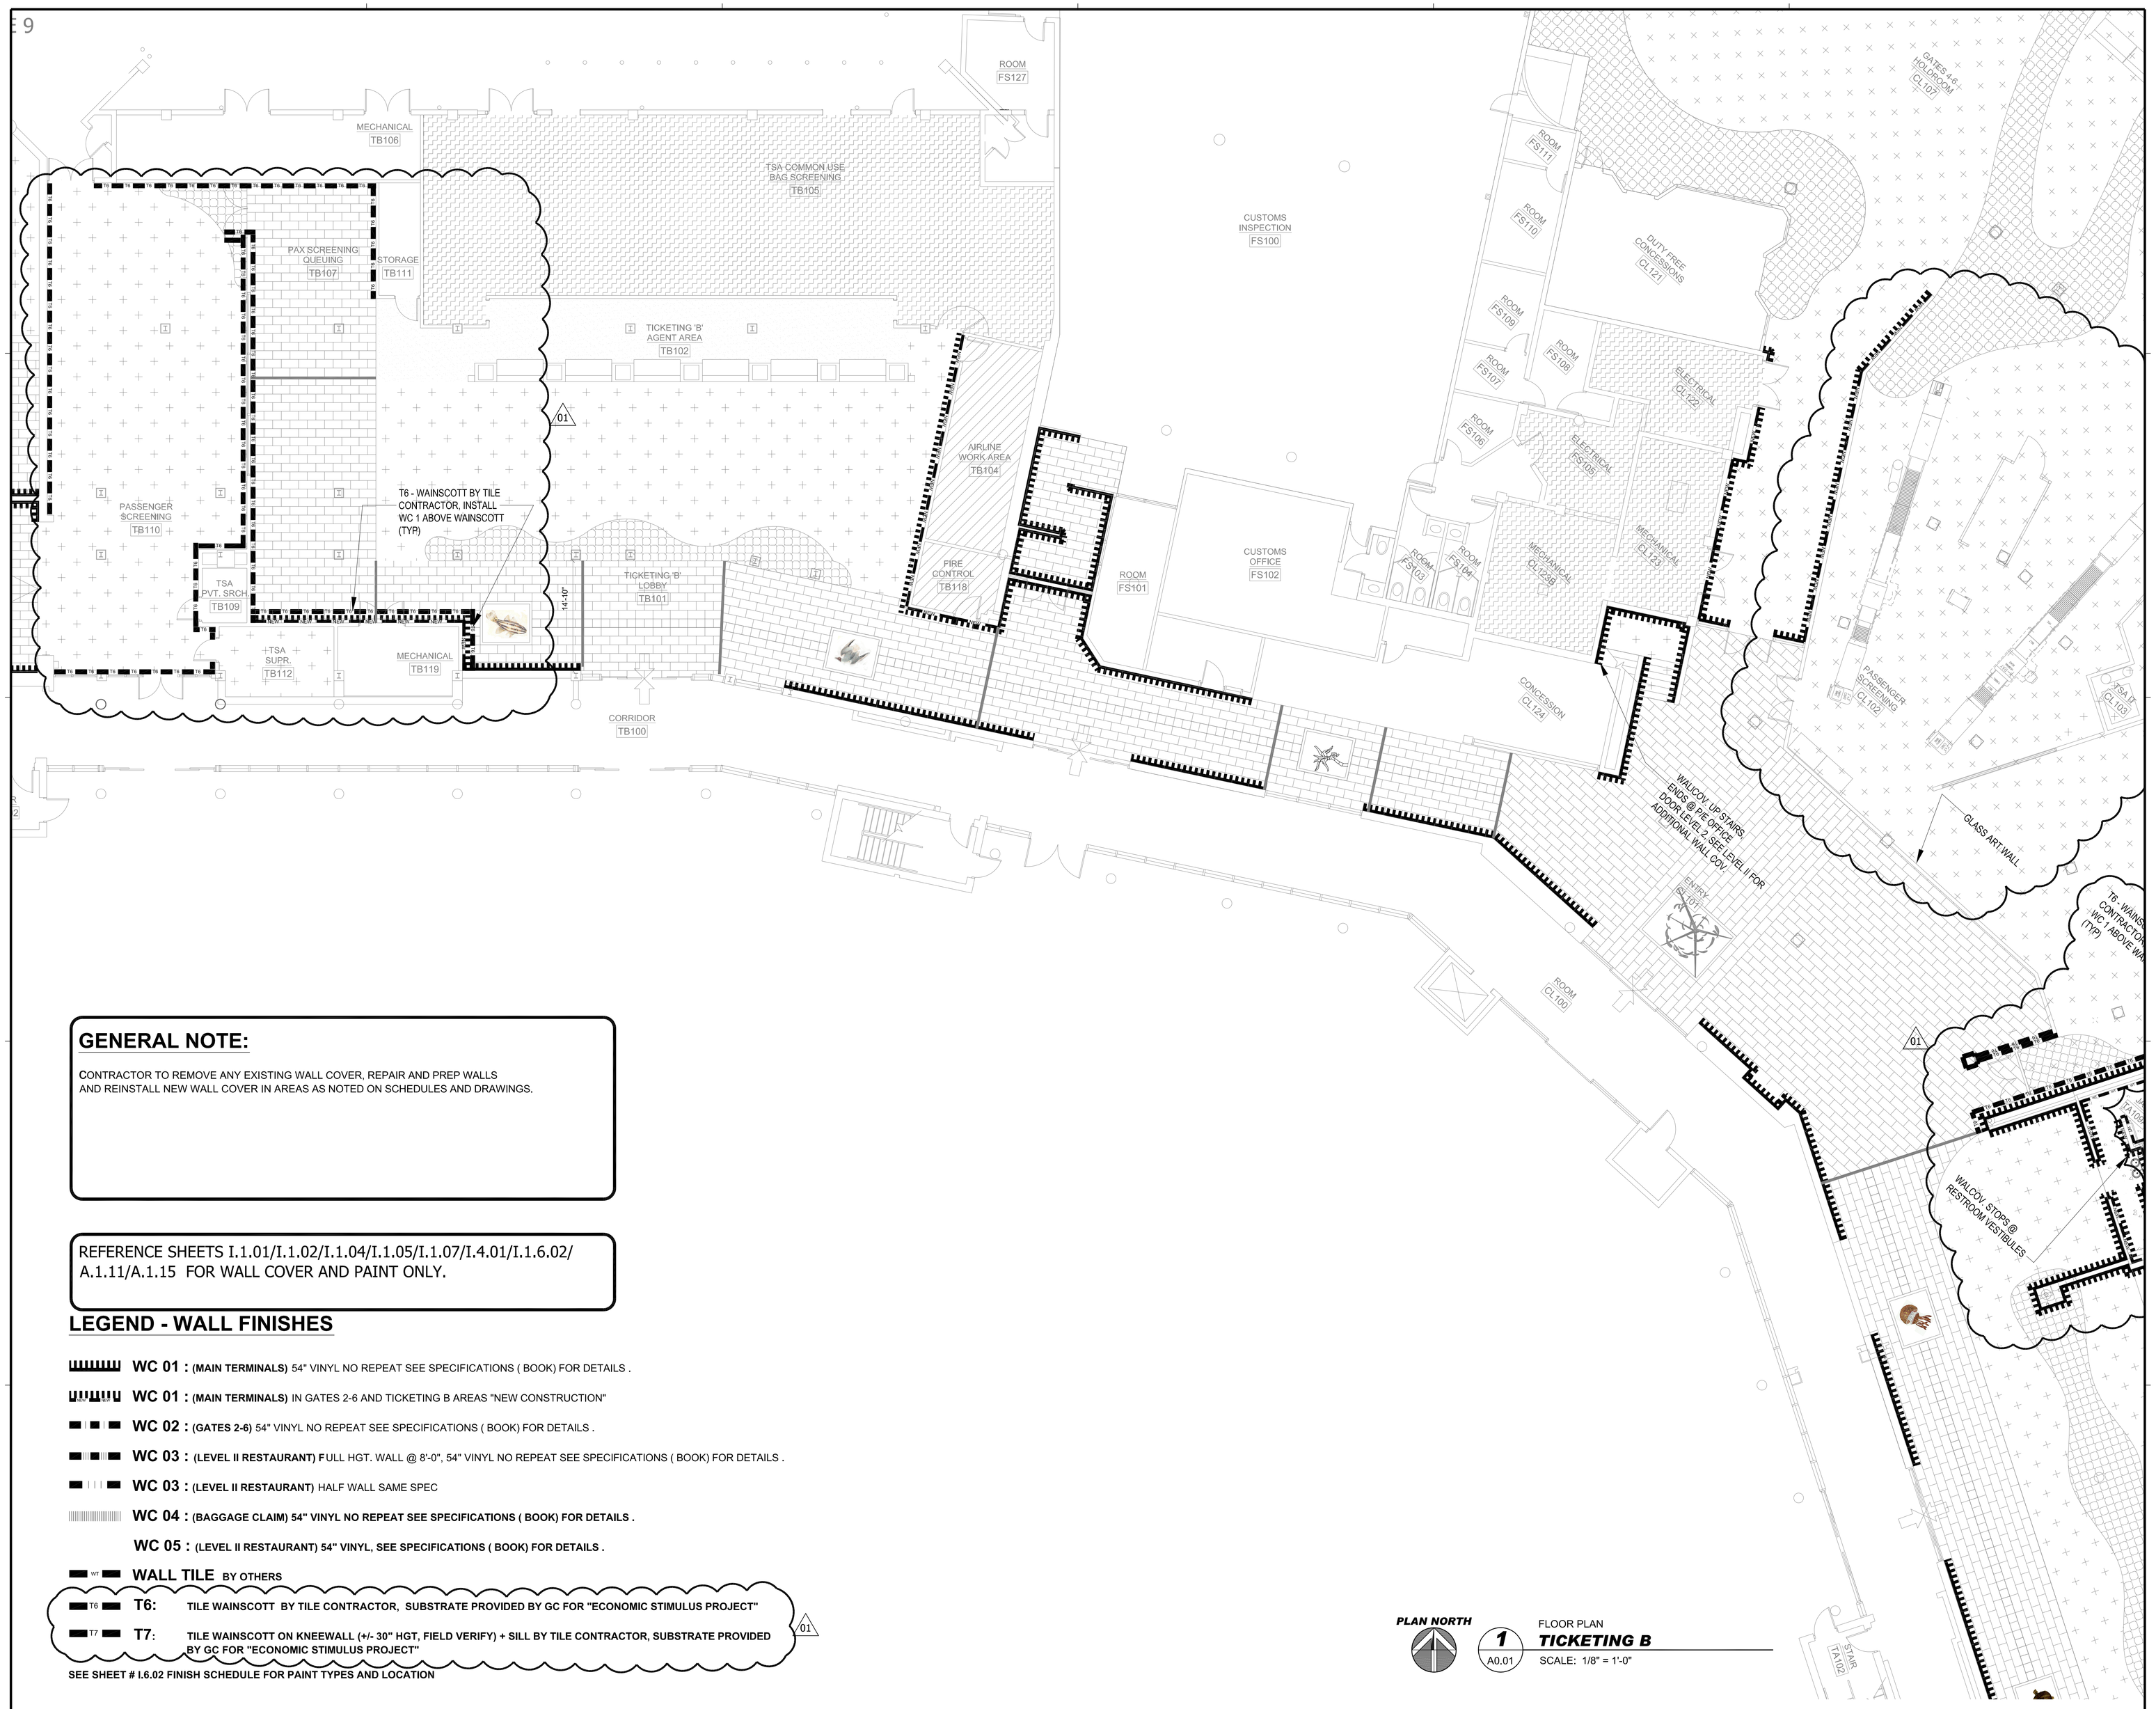

GENERAL NOTE:

CONTRACTOR TO REMOVE ANY EXISTING WALL COVER, REPAIR AND PREP WALLS AND REINSTALL NEW WALL COVER IN AREAS AS NOTED ON SCHEDULES AND DRAWINGS.

REFERENCE SHEETS I.1.01/I.1.02/I.1.04/I.1.05/I.1.07/I.4.01/I.1.6.02/ A.1.11/A.1.15 FOR WALL COVER AND PAINT ONLY.

LEGEND - WALL FINISHES

- **WC 01 : (MAIN TERMINALS)** 54" VINYL NO REPEAT SEE SPECIFICATIONS (BOOK) FOR DETAILS .
- **WC 01 : (MAIN TERMINALS)** IN GATES 2-6 AND TICKETING B AREAS "NEW CONSTRUCTION"
- **WC 02 : (GATES 2-6)** 54" VINYL NO REPEAT SEE SPECIFICATIONS (BOOK) FOR DETAILS .
- **WC 03 : (LEVEL II RESTAURANT)** FULL HGT. WALL @ 8'-0", 54" VINYL NO REPEAT SEE SPECIFICATIONS (BOOK) FOR DETAILS .
- **WC 03 : (LEVEL II RESTAURANT)** HALF WALL SAME SPEC
- **WC 04 : (BAGGAGE CLAIM) 54" VINYL NO REPEAT SEE SPECIFICATIONS (BOOK) FOR DETAILS .**
- **WC 05 : (LEVEL II RESTAURANT) 54" VINYL, SEE SPECIFICATIONS (BOOK) FOR DETAILS .**
- **WALL TILE** BY OTHERS
- **T6:** TILE WAINSCOTT BY TILE CONTRACTOR, SUBSTRATE PROVIDED BY GC FOR "ECONOMIC STIMULUS PROJECT"
- **T7:** TILE WAINSCOTT ON KNEEWALL (+/- 30" HGT, FIELD VERIFY) + SILL BY TILE CONTRACTOR, SUBSTRATE PROVIDED BY GC FOR "ECONOMIC STIMULUS PROJECT"

SEE SHEET # I.6.02 FINISH SCHEDULE FOR PAINT TYPES AND LOCATION

PLAN NORTH

1 A0.01 FLOOR PLAN **TICKETING B**
SCALE: 1/8" = 1'-0"

St. Petersburg Clearwater International Airport

THE LPA GROUP
ENGINEERS ARCHITECTS PLANNERS
700 HUGER STREET
COLUMBIA, SOUTH CAROLINA 29201
POST OFFICE BOX 5805
COLUMBIA, SOUTH CAROLINA 29250-5805
Phone: 803/254-2211 Fax: 803/779-0482
DENNIS J. WIEHL FLORIDA ARCHITECT LICENSE # 11995
LPA GROUP INCORPORATED FLORIDA LICENSE# AA00003054

KTD Inc.
KELLY TAAFFE DESIGN
Lic# ID 0002289
FL# 13 0001146
Kelly@kellytaaffedesign.com
Tel.: 813.695.5049
Fax: 813.805.2371

TERMINAL IMPROVEMENT PROJECT - WALL FINISHES

KEY PLAN



REVISIONS

No.	Description	Date	By
01	ADDENDUM 1	04/20/09	KTD

Designed by: | Drawn by: | Checked by:

Project Name:
TERMIAL IMPROVEMENT PROJECT WALL COVER & PAINT

Drawing Name:
FLOOR PLAN TICKETING B

LPA Project Number: AR178005.8
FAA AIP Project Number:
Date: 04 / 20/ 2009
Division :
Drawing Number: FP-ALL.dwg

I 1.04

TB-I1.04, 4/19/2009 2:39:03 PM
